




Browns Valley Trunk Project (CIP 14703) and West Napa Pump Station Project (CIP 17711) Update



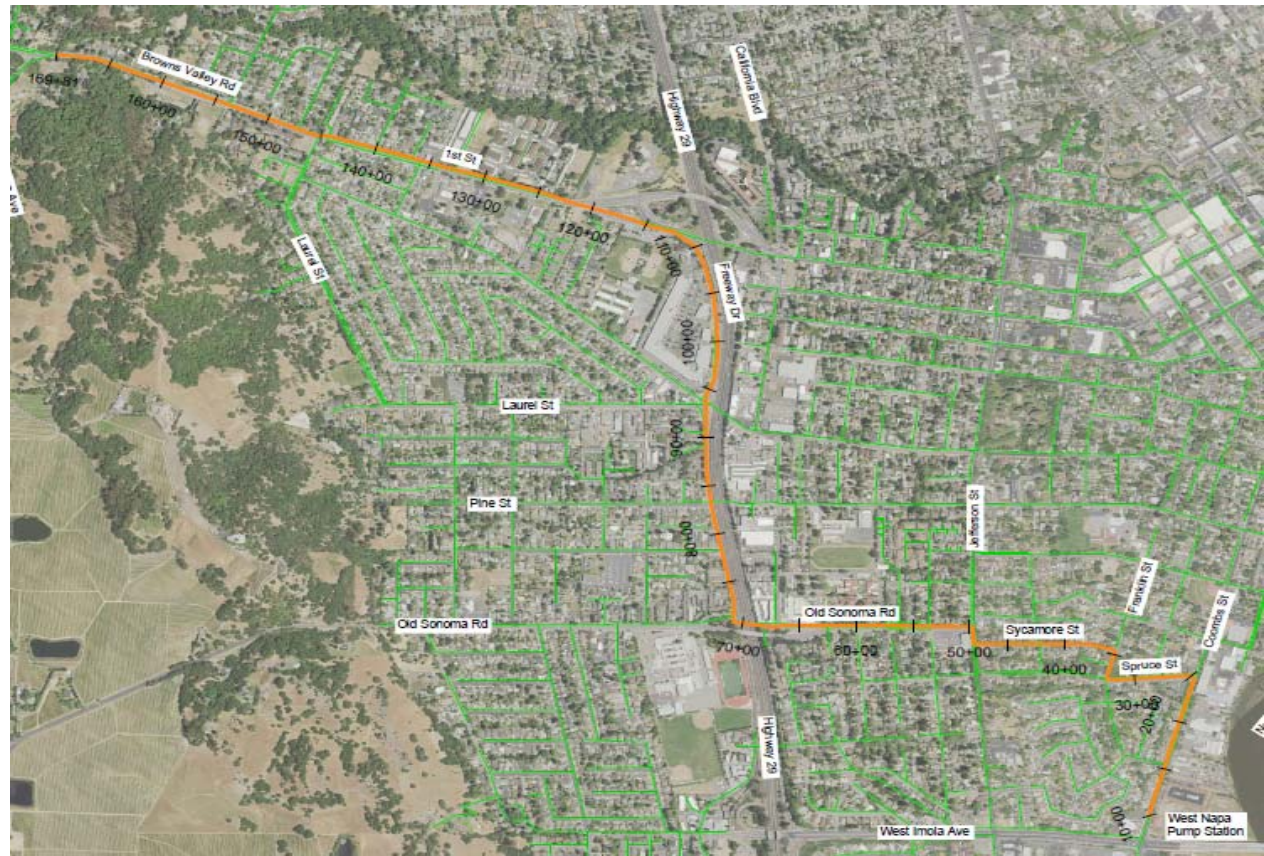

Contract Status

Item	BVT	WNPS
Original Contract	\$20,507,752	\$7,662,305
Total CO's	\$0	\$0
Total Contract	\$20,507,752	\$7,662,305
Paid to Date	\$0	\$207,504
Percent Remaining	100%	97%



Schedule

Item	BVT	WNPS Pump Station	WNPS Overall Project
Notice to Proceed	March 30, 2020	March 30, 2020	March 30, 2020
Contract Days	560	489	574
Days Remaining	498	427	512
Substantial Completion (Est)	October 11, 2021	August 1, 2021	October 25, 2021
Percent of Days Expired	11%	13%	11%



May Activities

BVT	WNPS
Mobilization	Mobilization
Survey	SWPPP
Potholing	Utility Locating
Utility Locating	





Outreach Map





Any Questions?
