


ID	Task Name	Duration	Start	Finish	Resource Names	6/1/20							6/8/20							6/15/20							6/22/20						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	S Coombs St Staging Area	35 days	Mon 6/1/20	Fri 7/17/20		[Gantt bar for S Coombs St Staging Area]																											
2	Temporary Power & Internet	4 days	Tue 6/9/20	Fri 6/12/20		[Gantt bar for Temporary Power & Internet]																											
3	PG&E Service & Meter Installation (Confirmed Date)	1 day	Tue 6/9/20	Tue 6/9/20	PG&E	[Gantt bar for PG&E Service & Meter Installation]																											
4	Install Internet Service through Temp Power Pole	2 days	Thu 6/11/20	Fri 6/12/20	JMB / Comcast	[Gantt bar for Install Internet Service]																											
5	Material Deliveries	35 days	Mon 6/1/20	Fri 7/17/20		[Gantt bar for Material Deliveries]																											
6	48" PVC Piping (1ea Load/Day at 84ft/Load)	20 days	Mon 6/1/20	Fri 6/26/20	Ferguson	[Gantt bar for 48" PVC Piping]																											
7	30" PVC Piping (1ea Load)	5 days	Mon 6/1/20	Fri 6/5/20	Ferguson	[Gantt bar for 30" PVC Piping]																											
8	24" PVC Piping (1ea Load)	5 days	Mon 6/1/20	Fri 6/5/20	Ferguson	[Gantt bar for 24" PVC Piping]																											
9	15" PVC Piping (1ea Load)	5 days	Mon 6/1/20	Fri 6/5/20	Ferguson	[Gantt bar for 15" PVC Piping]																											
10	SSMH No 1 & 2 Precast Assembly (1-2ea Loads)	10 days	Mon 6/15/20	Fri 6/26/20	Armorock	[Gantt bar for SSMH No 1 & 2 Precast Assembly]																											
13	Staking	5 days	Mon 6/15/20	Fri 6/19/20		[Gantt bar for Staking]																											
14	Offsets/Cuts Staking along S Coombs St	5 days	Mon 6/15/20	Fri 6/19/20	F3	[Gantt bar for Offsets/Cuts Staking]																											
15	Utilitiy Locating	18 days	Mon 6/8/20	Wed 7/1/20		[Gantt bar for Utilitiy Locating]																											
16	USA Utility Marking along S Jefferson/Old Sonoma Rd	5 days	Mon 6/8/20	Fri 6/12/20	Various	[Gantt bar for USA Utility Marking]																											
17	Centerline Marking along Freeway Dr to Laurel / Kilbur	2 days	Mon 6/15/20	Tue 6/16/20	JMB	[Gantt bar for Centerline Marking]																											
18	USA Utility Marking along Freeway Dr to Laurel / Kilbur	4 days	Wed 6/17/20	Mon 6/22/20	Various	[Gantt bar for USA Utility Marking]																											
19	Centerline Marking along Freeway Dr to First St	2 days	Tue 6/23/20	Wed 6/24/20	JMB	[Gantt bar for Centerline Marking]																											
20	USA Utility Marking along Freeway Dr to First St	5 days	Thu 6/25/20	Wed 7/1/20	Various	[Gantt bar for USA Utility Marking]																											
21	Potholing / Pre Characterization Work	23 days	Mon 6/1/20	Wed 7/1/20		[Gantt bar for Potholing / Pre Characterization Work]																											
22	Pre-Characterization Samples Analysing	5 days	Mon 6/1/20	Fri 6/5/20	McC Campbell	[Gantt bar for Pre-Characterization Samples]																											
23	Pothole Ex Utilities along S Coombs St (approx 30ea)	2 days	Mon 6/1/20	Tue 6/2/20	JMB	[Gantt bar for Pothole Ex Utilities S Coombs St]																											
24	Pothole Ex Utilities along Spruce St (approx 20ea)	3 days	Wed 6/3/20	Fri 6/5/20	JMB	[Gantt bar for Pothole Ex Utilities Spruce St]																											
25	Pothole Ex Utilities along Franklin St (approx 5ea)	1 day	Mon 6/15/20	Mon 6/15/20	JMB	[Gantt bar for Pothole Ex Utilities Franklin St]																											
26	Pothole Ex Utilities along Sycamore St (approx 40ea)	7 days	Tue 6/16/20	Wed 6/24/20	JMB	[Gantt bar for Pothole Ex Utilities Sycamore St]																											
27	Pothole Ex Utilities along S Jefferson St (approx 5ea)	2 days	Thu 6/25/20	Fri 6/26/20	JMB	[Gantt bar for Pothole Ex Utilities S Jefferson St]																											
29	Waterline Work along S Coombs St	11 days	Fri 6/5/20	Fri 6/19/20		[Gantt bar for Waterline Work]																											
30	Exc/Prep All Water Service Tie Ins	2 days	Fri 6/5/20	Mon 6/8/20		[Gantt bar for Exc/Prep All Water Service Tie Ins]																											
31	Installing All Water Services Tie Ins	3 days	Mon 6/8/20	Wed 6/10/20	City of Napa	[Gantt bar for Installing All Water Services Tie Ins]																											
32	Install 4ea 1in to 2in Services	1 day	Wed 6/10/20	Wed 6/10/20	JMB	[Gantt bar for Install 4ea 1in to 2in Services]																											
33	Install new Fire Hydrant Line	2 days	Thu 6/11/20	Fri 6/12/20	JMB	[Gantt bar for Install new Fire Hydrant Line]																											
34	Connect 4ea 1in to 2in Services to Meters	1 day	Wed 6/17/20	Wed 6/17/20	JMB	[Gantt bar for Connect 4ea 1in to 2in Services to Meters]																											
35	Abandon existing Water Main	0 days	Wed 6/17/20	Wed 6/17/20	City of Napa	[Gantt bar for Abandon existing Water Main]																											
36	Install 4in Water Service & 8in Fire Service	2 days	Thu 6/18/20	Fri 6/19/20	JMB	[Gantt bar for Install 4in Water Service & 8in Fire Service]																											
37	Mainline Piping Installation	5 days	Mon 6/22/20	Fri 6/26/20		[Gantt bar for Mainline Piping Installation]																											
38	SSMH No. 1 / 48" PVC Piping Planned Start Date	0 days	Mon 6/22/20	Mon 6/22/20	JMB ML Crew	[Gantt bar for SSMH No. 1 / 48" PVC Piping Planned Start Date]																											
39	Sawcut Trench	4 days	Mon 6/22/20	Thu 6/25/20	JMB ML Crew	[Gantt bar for Sawcut Trench]																											
40	Setup Dewatering Equipment	2 days	Mon 6/22/20	Tue 6/23/20	JMB ML Crew	[Gantt bar for Setup Dewatering Equipment]																											
41	Commence 48" Piping Installation from SSMH #1	3 days	Wed 6/24/20	Fri 6/26/20	JMB ML Crew	[Gantt bar for Commence 48" Piping Installation]																											

Project: NSD BVT Date: Tue 6/9/20	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			



BROWN VALLEY TRUNK PROJECT
 BVT ALIGNMENT: ———

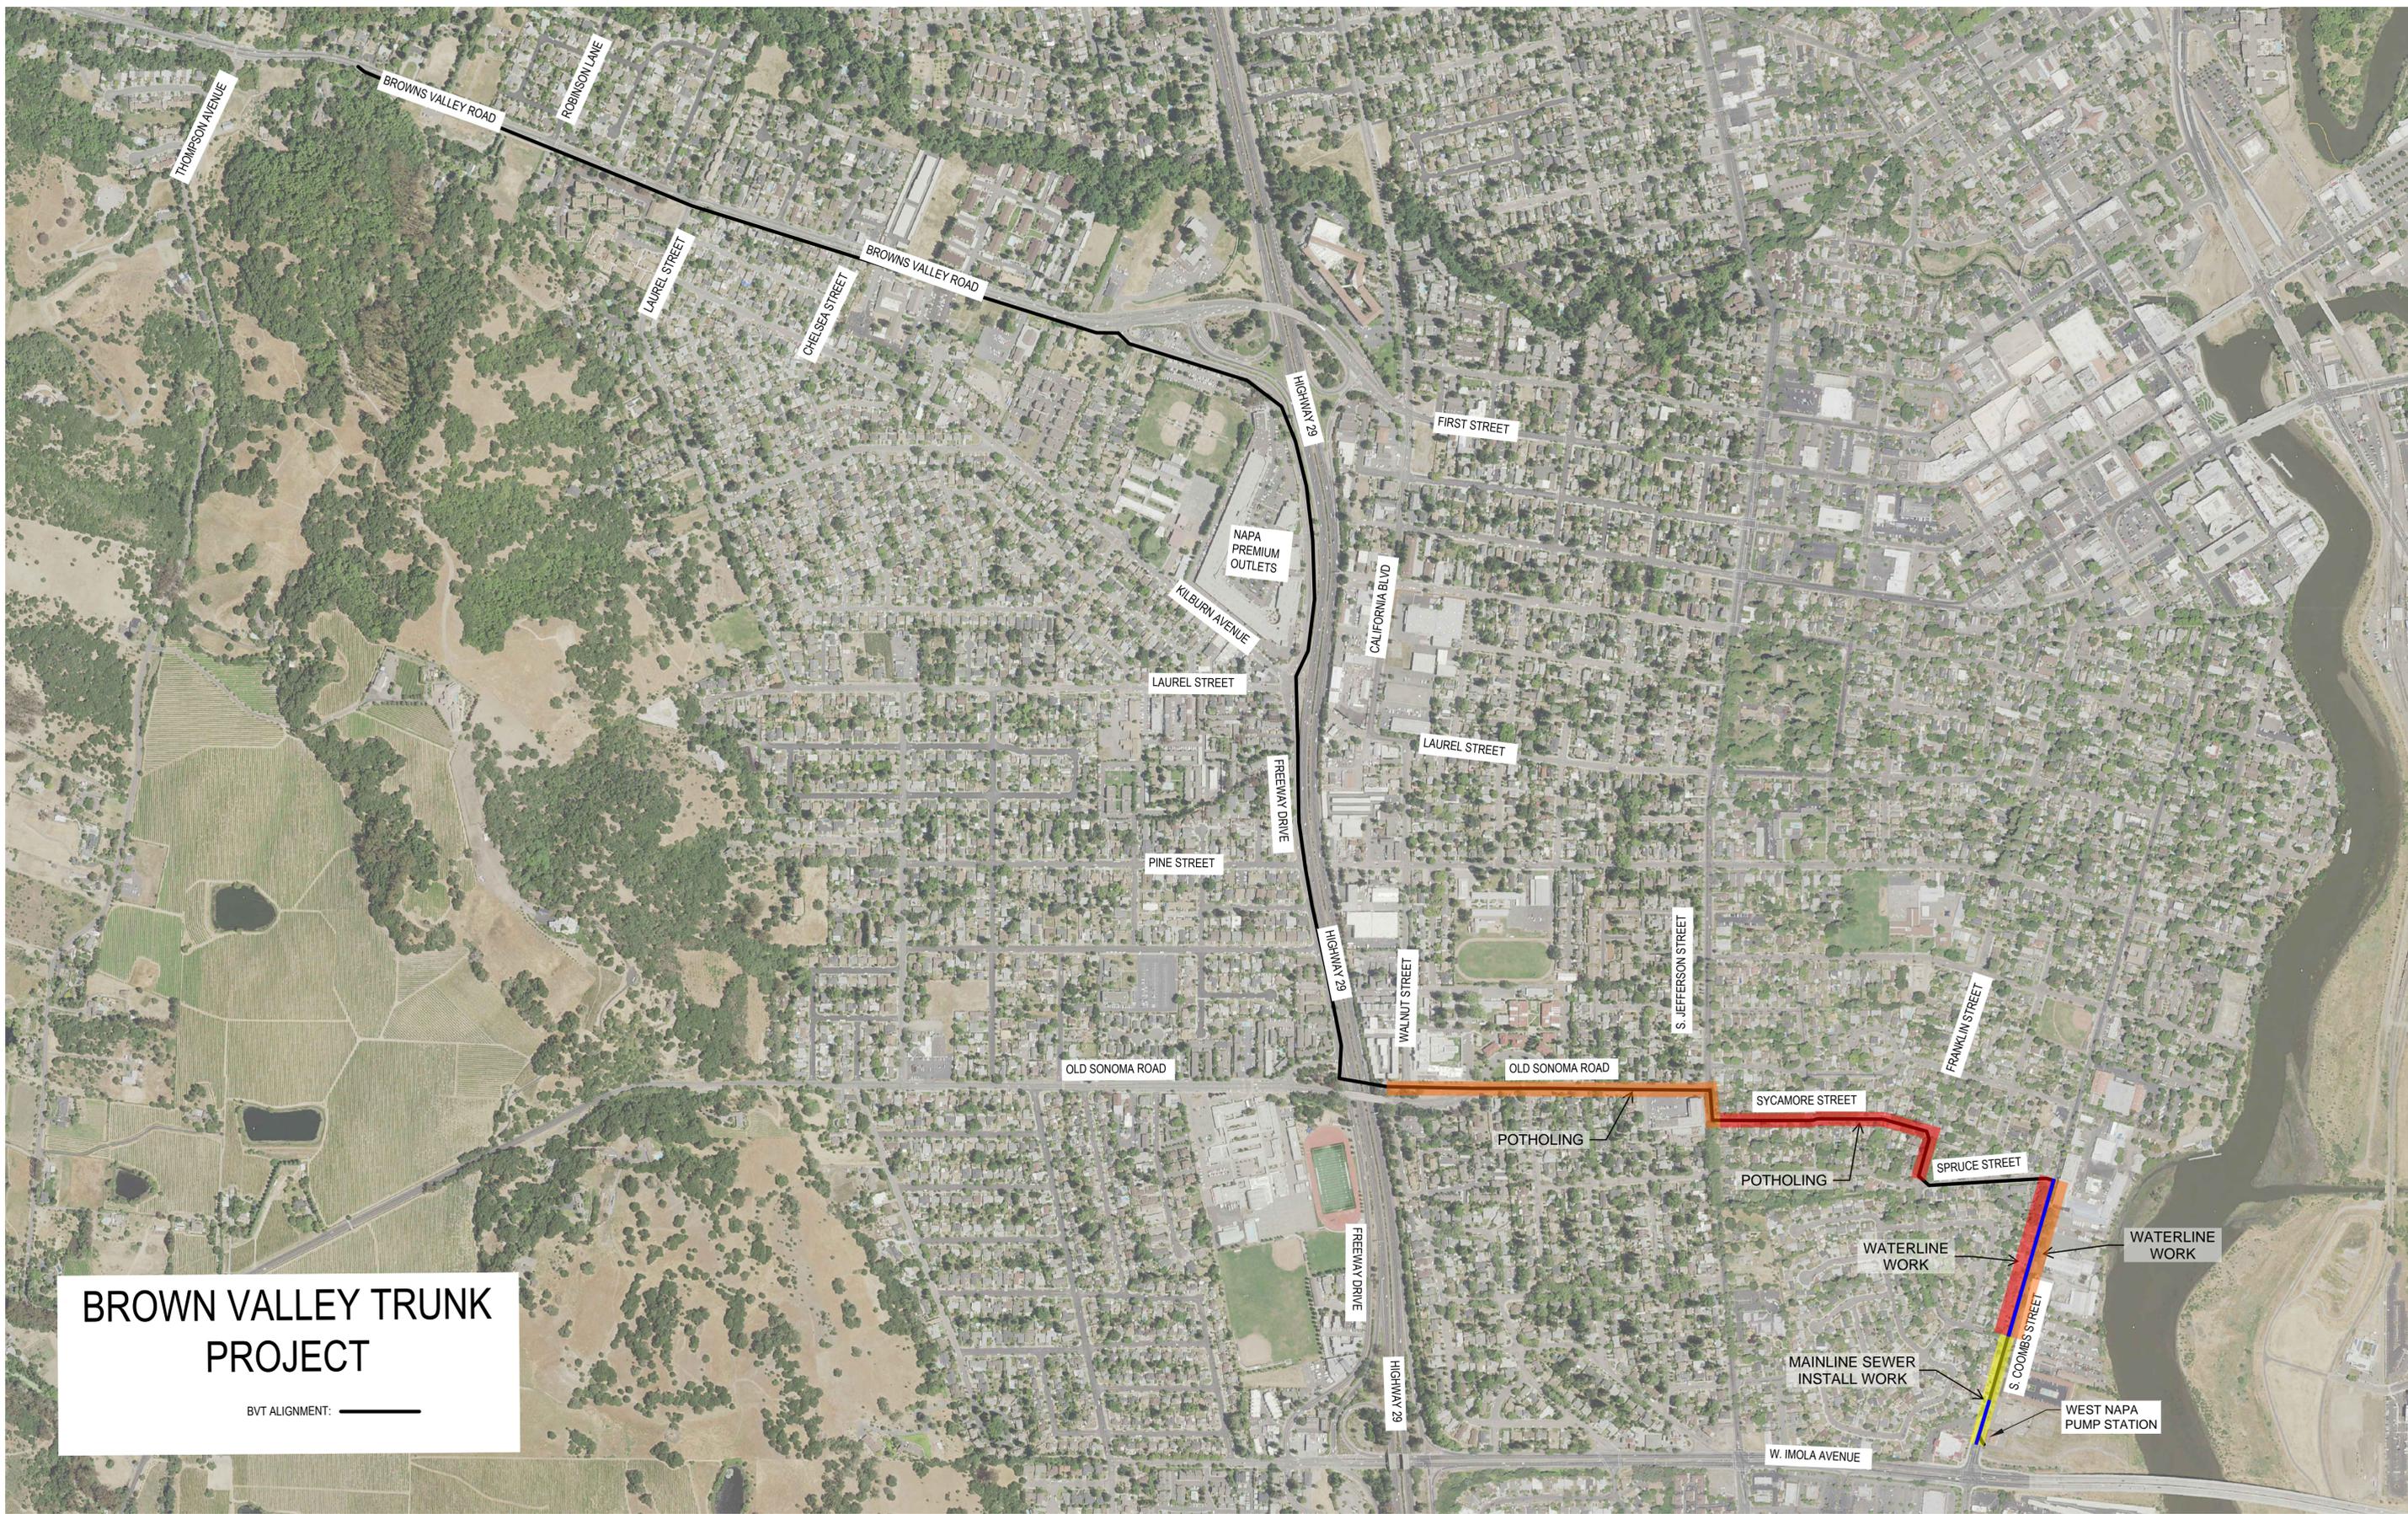
