




Basin "L" Pipeline Rehabilitation Project #5 (CIP 16701)






Primary Project Locations

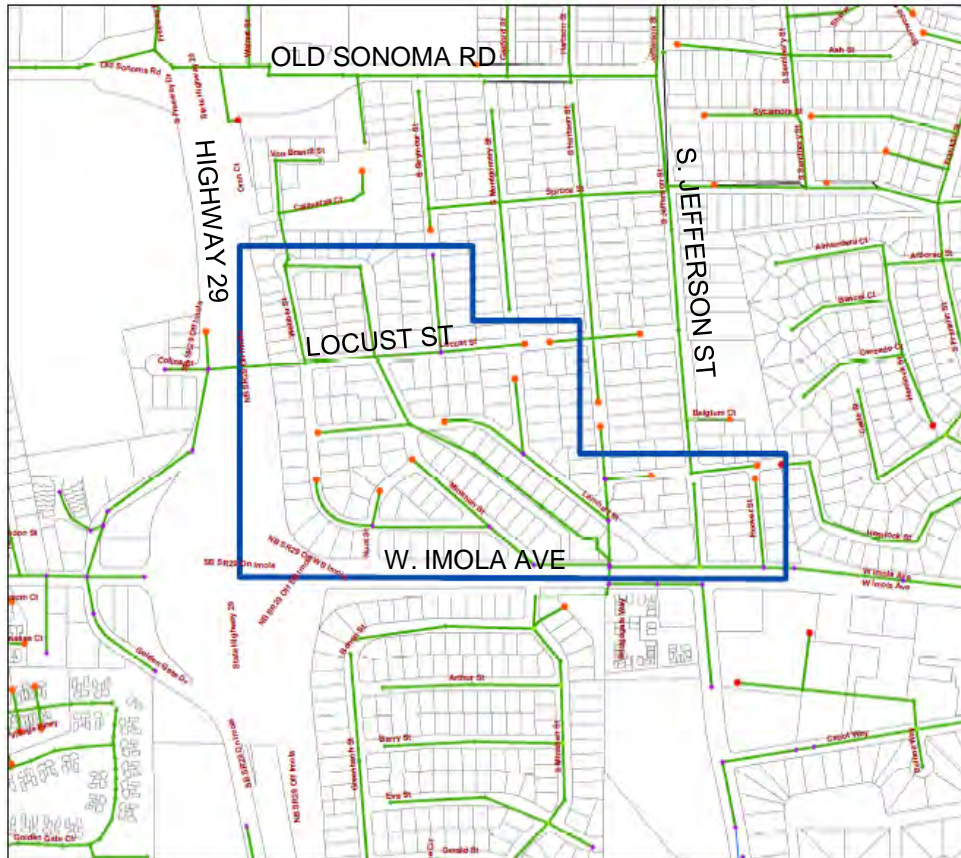




Added Project Locations – Maple St.

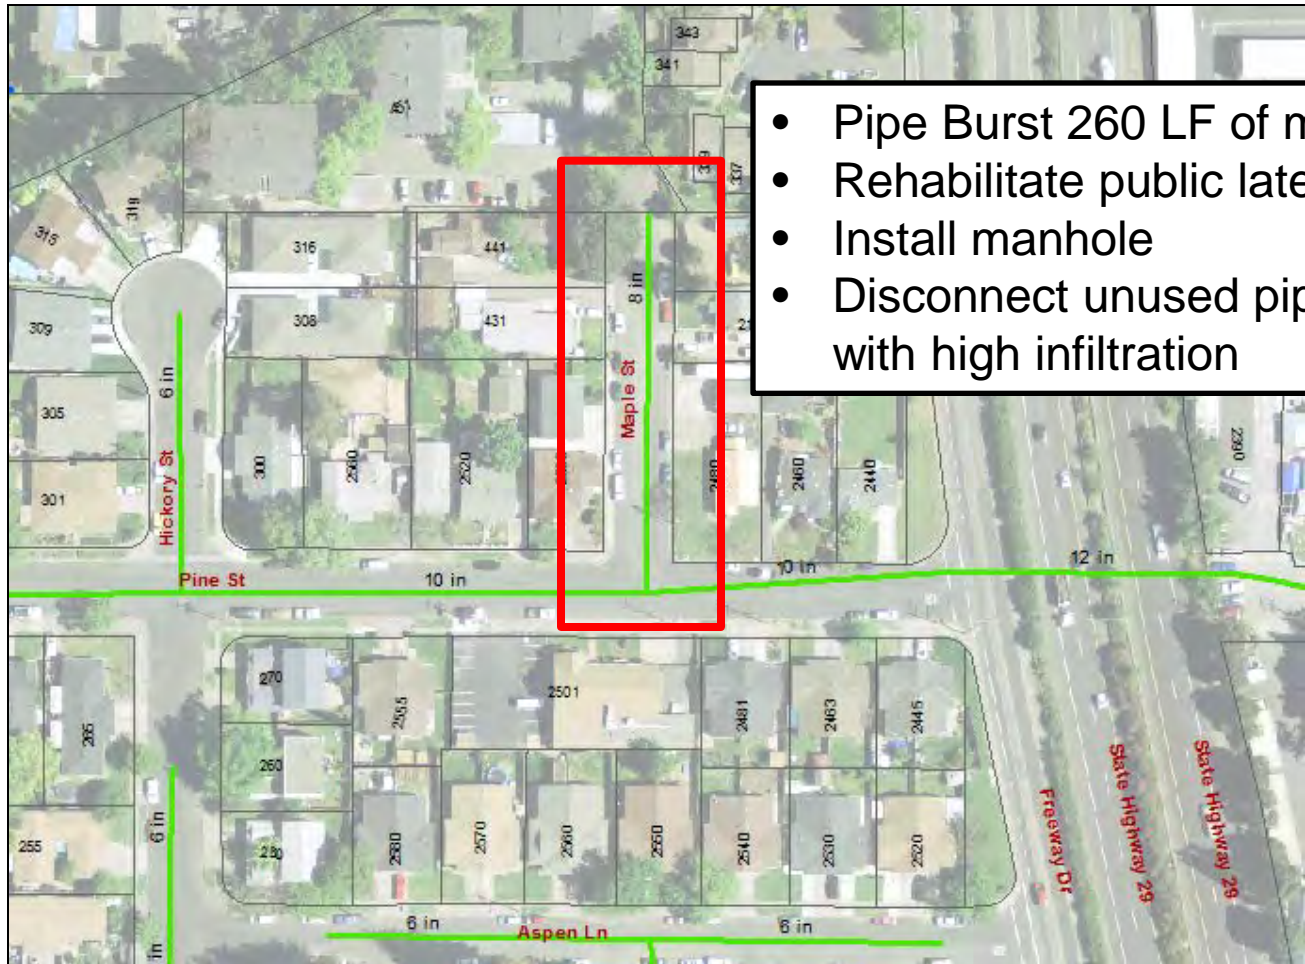

- Pipe Burst 260 LF of main
- Rehabilitate public laterals
- Install manhole
- Disconnect unused pipe with high infiltration



Added Project Locations – Young Ave.

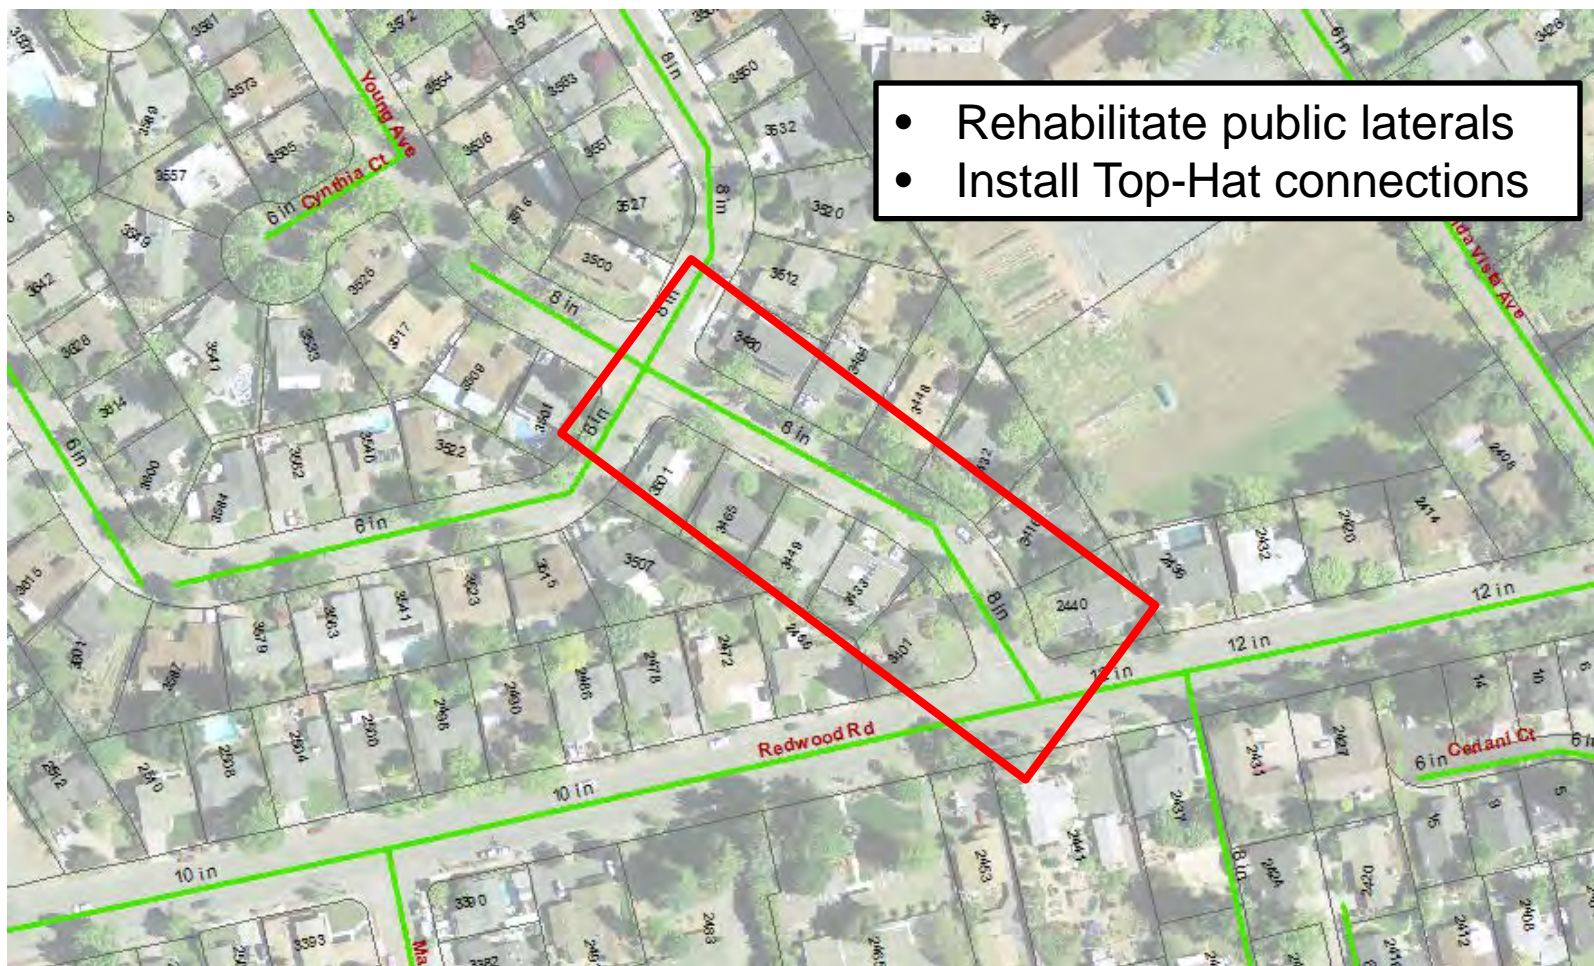




Accomplishments

- Rehabilitate/Replace Collection System Assets
 - 1.5 miles of sewer main
 - 108 public sewer laterals
 - 18 sewer manholes/flush holes
- Decrease Inflow/Infiltration
- Coordination with Caltrans
- Coordination with City Water and SD projects
- Complete project prior to City paving
- Abandon backyard main
- Coordination with businesses and residents



Backyard Main Abandonment

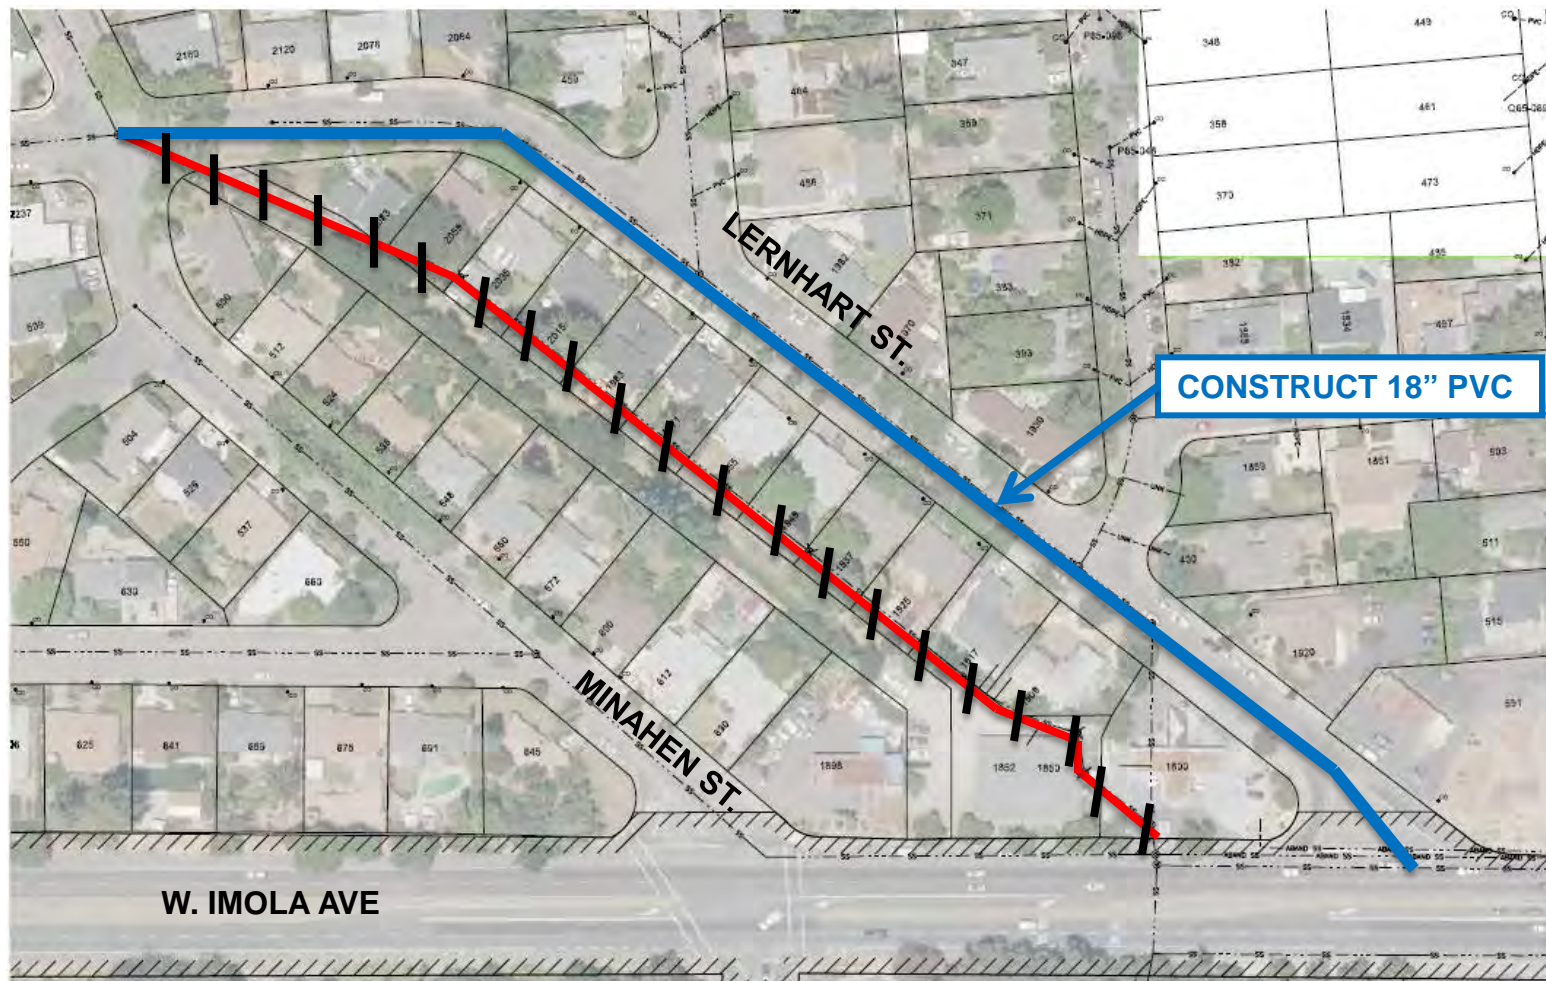



Costs

- Engineer's Estimate \$2,400,000
- Low Bid \$1,819,954
- Change orders \$42,396
(2.3%)
- Final contract amount \$1,862,350
- Change orders were owner-initiated and added scope to the project



Recommendation

- Adopt Resolution accepting completion and authorize the General Manager to file Notice of Completion with the County Recorder
